



Switchyard Shutdown 2017 Week 5

Adam Watts
0900 Meeting
8/11/17

Cable Mitigation

Cable wrapping (hazard mitigation) is complete in Transfer Hall, M01, M02, M03, and M05.

Documentation of mitigated cables is still the focus. Transfer Hall, M03, M05 remain.


Switch from Booster 95 to F-sector LCW

Pipe-fitters finished connection into Transfer Hall piping.

Cut both holes in Enclosure B piping for saddle joint tie-ins. Welded and completed one tie-in, and will complete the other today.

Will give estimate this afternoon as to time needed for remainder of the job.

We have decided on the “Secondary Plan” as pictured below, which is where the saddle joint tie-ins have been placed.

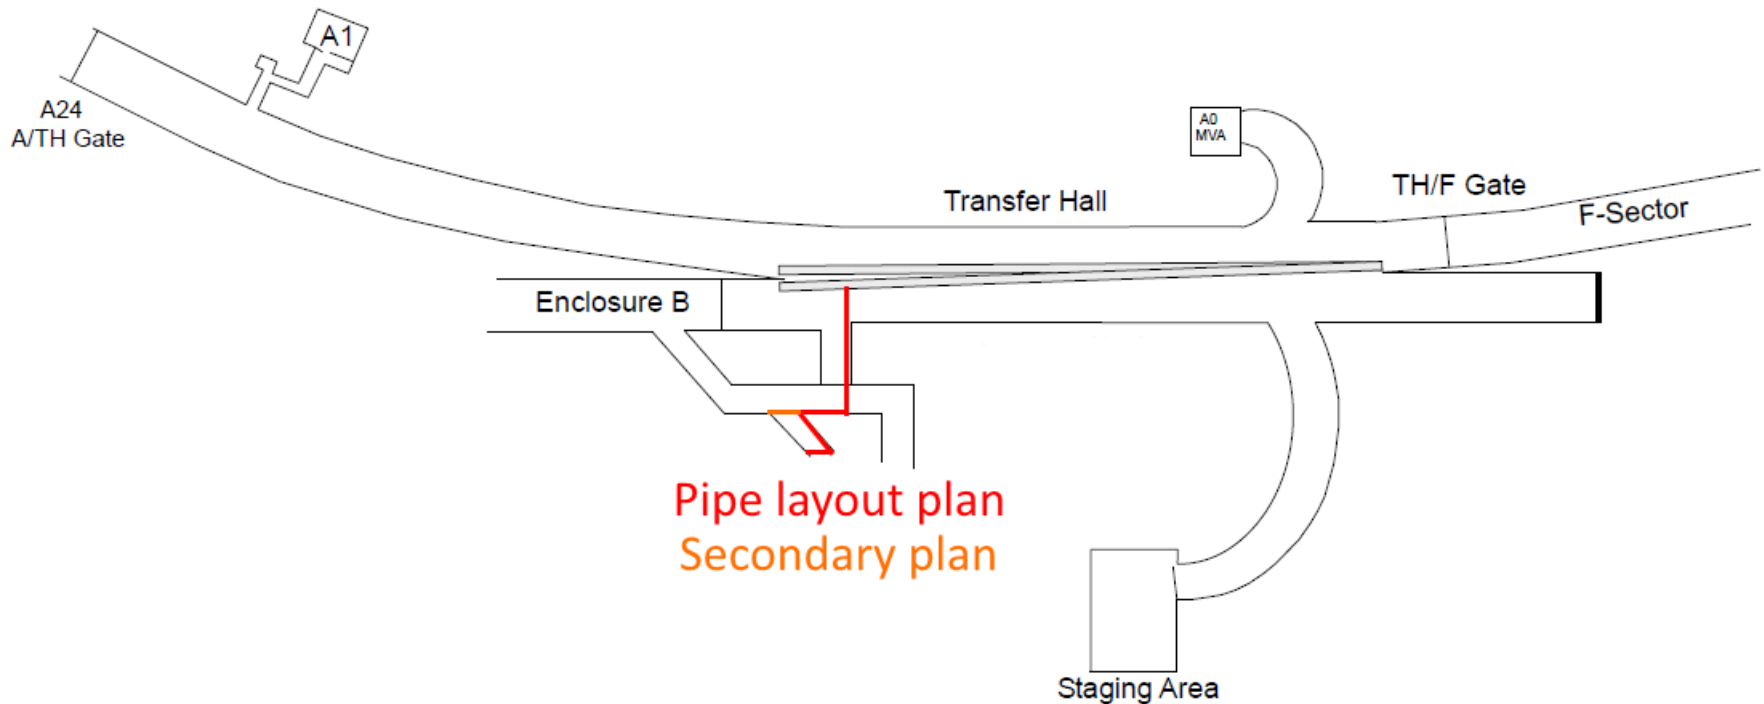

F-3 sector vacuum upgrade

EE support (Sievert) is refurbishing/modifying TeV CIA crate for use in F3 (new processor, backplane, wire-wrapping, etc.), same as they did for F4 last summer.

Will continue into next week.

Cable terminations and installing CIA crate to follow.

MS2LCW PLC upgrade

Fluids group have installed all of their sensors.

Controls group have all PLC parts delivered. Working on drawings for sub-panel to hold PLC and cable terminations in MS2.
