



# Switchyard Shutdown 2017 Week 6

Adam Watts  
0900 Meeting  
8/18/17

# Cable Mitigation

Documentation of mitigated cables is still the focus. Transfer Hall, M05 remain.

# Switch from Booster 95 to F-sector LCW

Pipe now along hallway from Transfer Hall to Enclosure B.


Tie-in at Enclosure B with valves complete.

Connecting up middle part in Enclosure B remains.

Welder switched to larger-diameter feed rod for Stainless welds, improved efficiency:

Usual pace was ~2 hours per weld, decreased to a bit over an hour.

Pipe-fitting job will be complete middle of Week 8.

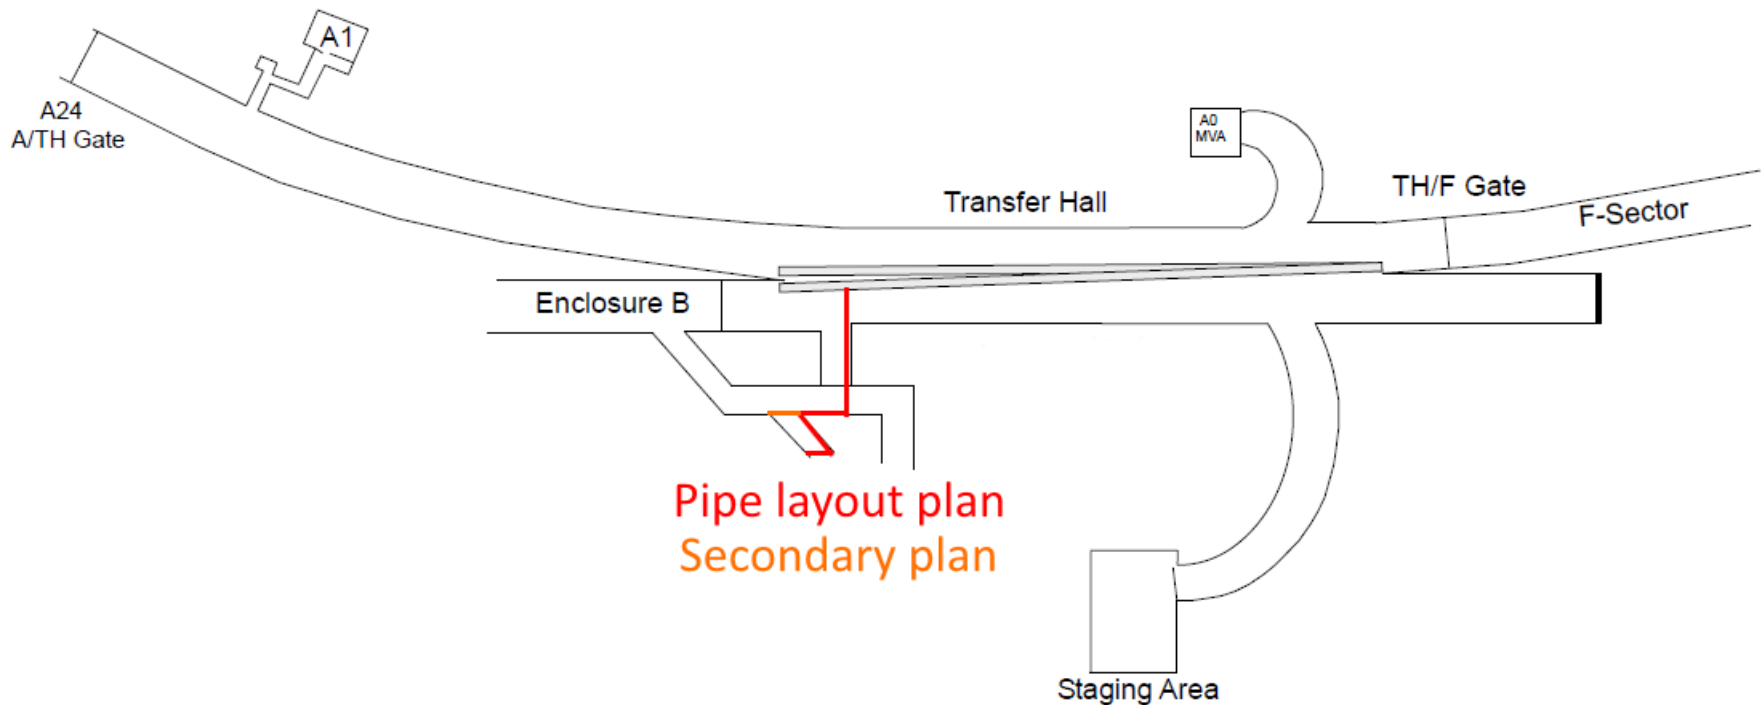

# F-3 sector vacuum upgrade

EE support (Sievert) is refurbishing/modifying TeV CIA crate for use in F3 (new processor, backplane, wire-wrapping, etc.), same as they did for F4 last summer.

# MS2LCW PLC upgrade

Controls will start working @ end of month on drawings for sub-panel to hold PLC and cable terminations in MS2.
