



# Switchyard Shutdown 2017 Week 9


Adam Watts  
0900 Meeting  
9/8/17

# Cable Mitigation

Documentation of mitigated cables is still the focus. Transfer Hall remains, need to finish up area where pipe-fitters have been working once they've vacated.

# Switch from Booster 95 to F-sector LCW

Looks like pipe installation should be finished by end of today. Pipe-fitters gave estimate this morning of end of Monday (lots of equipment to remove from tunnel, clean-up, etc.)

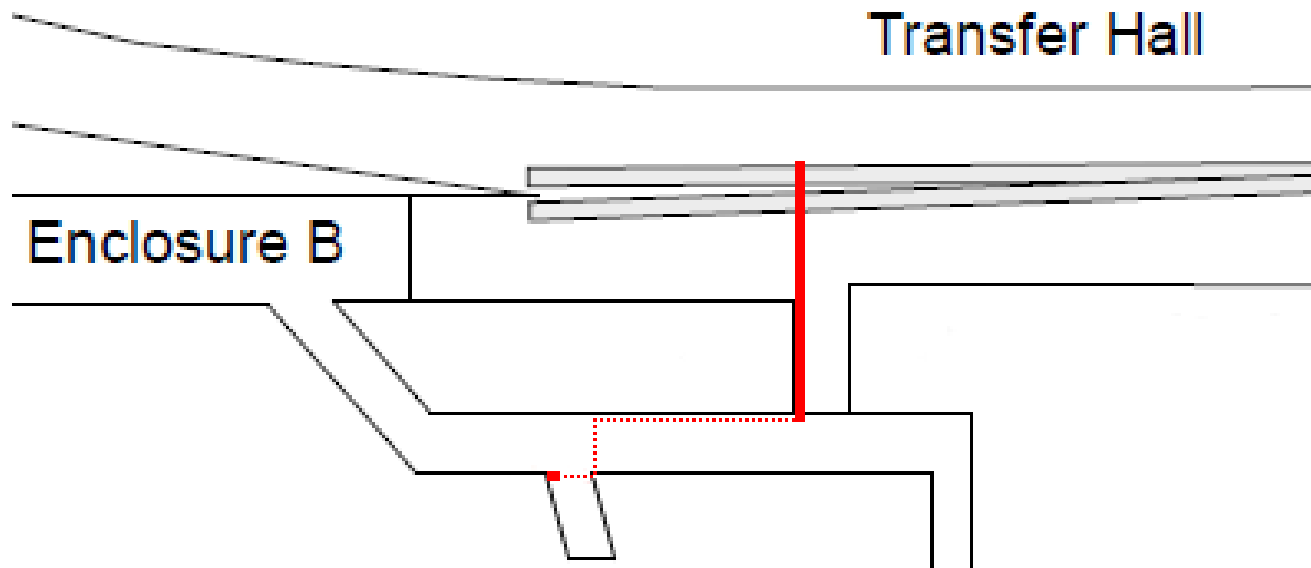

Pipe layout plan

# F-3 sector vacuum upgrade

EE support (Sievert) is finished installing the modified CIA crate, and the PiVac crate controller is installed.

Left to do:

- Install 120 V outlets near roughers in F3 and F4 for anti-suckback valve power.
- Update vacuum page to reflect new configuration.

# MS2LCW PLC upgrade

Interface box wiring finished.

After MI-65 work is finished, Controls will start working on PLC sub-panel fabrication.
