



Switchyard Shutdown 2017 Week 3

Adam Watts
0900 Meeting
7/28/17

Cable Mitigation

Some cable wrapping remains in Transfer Hall, once pipe-fitters are finished working in the area.


Documentation of mitigated cables is still the focus, almost finished with M02. Transfer Hall, M03, M05 remain.

Switch from Booster 95 to F-sector LCW

Still deciding which is safest plan: original layout plan or secondary (original plan reduces width of walkway).

Contractors installed pipe support anchors into the wall in Enclosure B. Working on installing second pipe along ceiling in Transfer Hall.

Thanks to FESS for relamping critical area and loaning work lights!


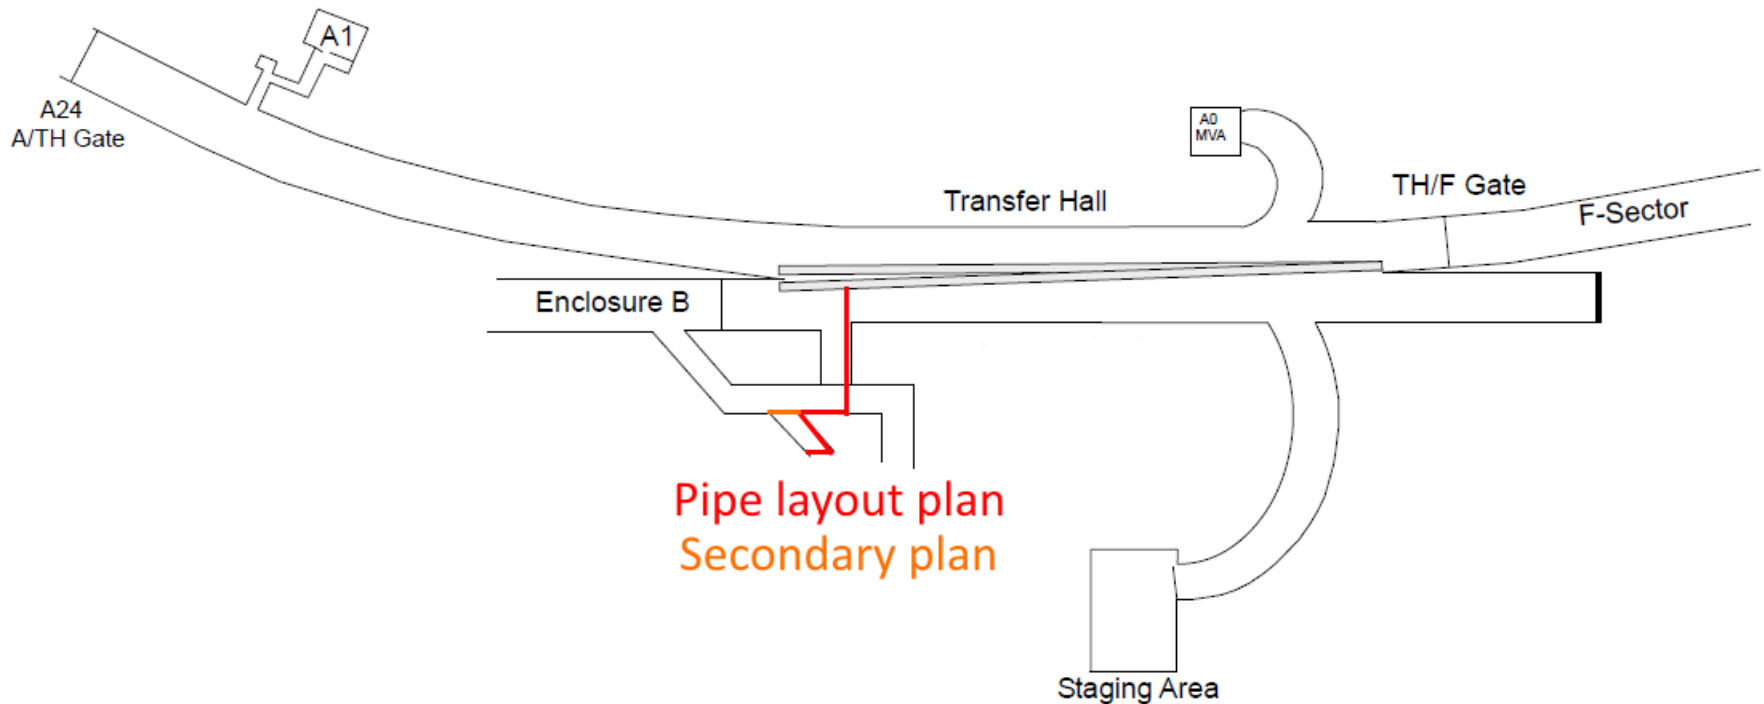


F-3 sector vacuum upgrade

FESS disconnected electricity to old ion pump rack and old rougher pump Rack and old rougher moved to make room for new roughers.

New roughers installed, piped in to roughing line, everything leak checked.

Controls work is remaining (re-installing CIA crate w/ PiVac, terminating and connecting cables)

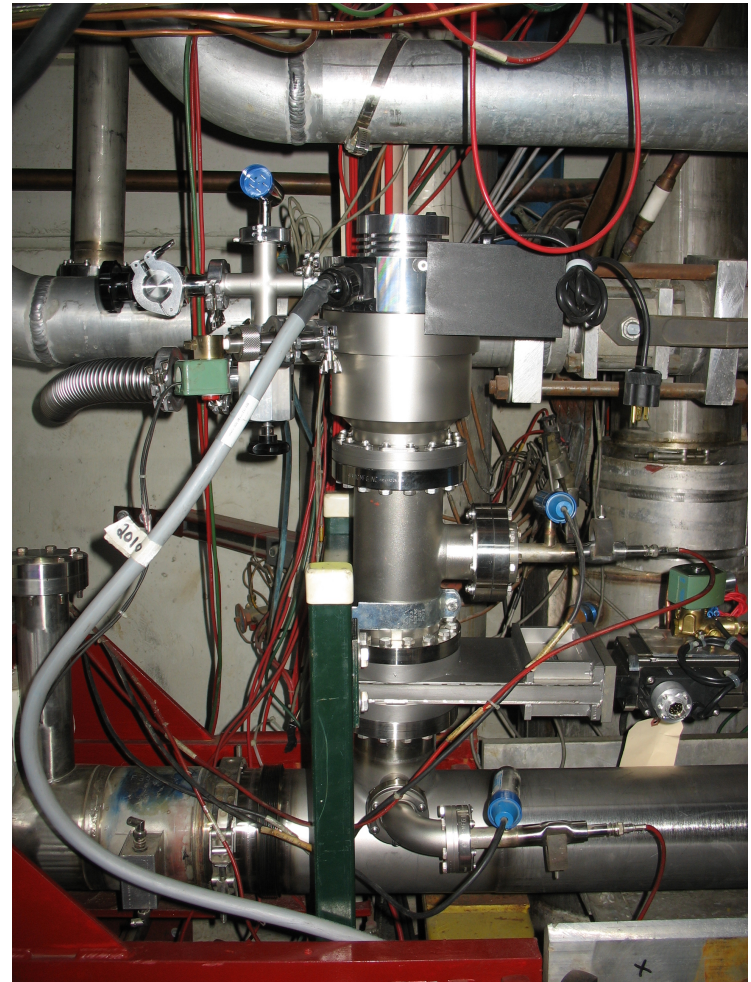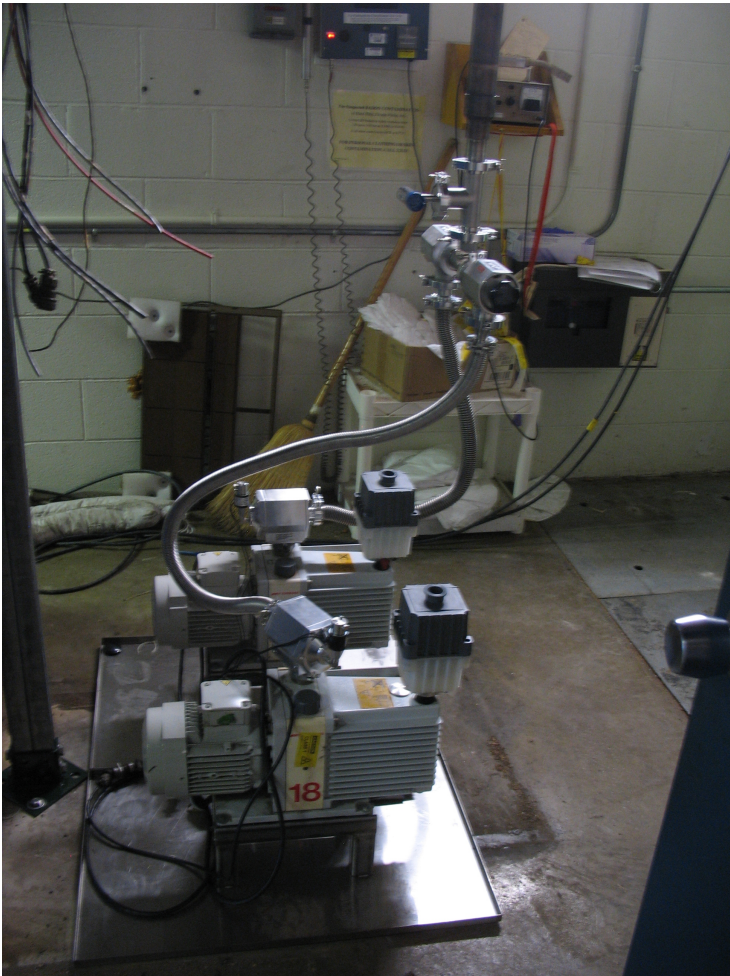

MS2LCW PLC upgrade

Fluids group have installed all of their sensors.

Controls group have received all PLC parts. Working on drawings for sub-panel to hold PLC and cable terminations in MS2.
