


# *Status of PMT cabling*

*Gian Luca Raselli  
INFN - Pavia*

*WA104 meeting, 06-NOV-2019*

# PMT Cabling Status

- Completed the cabling of the WW TPC (9 HV + 9 BNC flanges).
- On going the cabling of the WE TPC (4 HV + 4 BNC missing):
  - The cable deployment was stopped yesterday because of a fire alarm and a shortage of ladders.
- Two HV + two BNC flanges are presently cabled in the EW TPC.
- Two HV + two BNC flanges are presently cabled in the EW TPC.
- We are presently at 50% of the work.

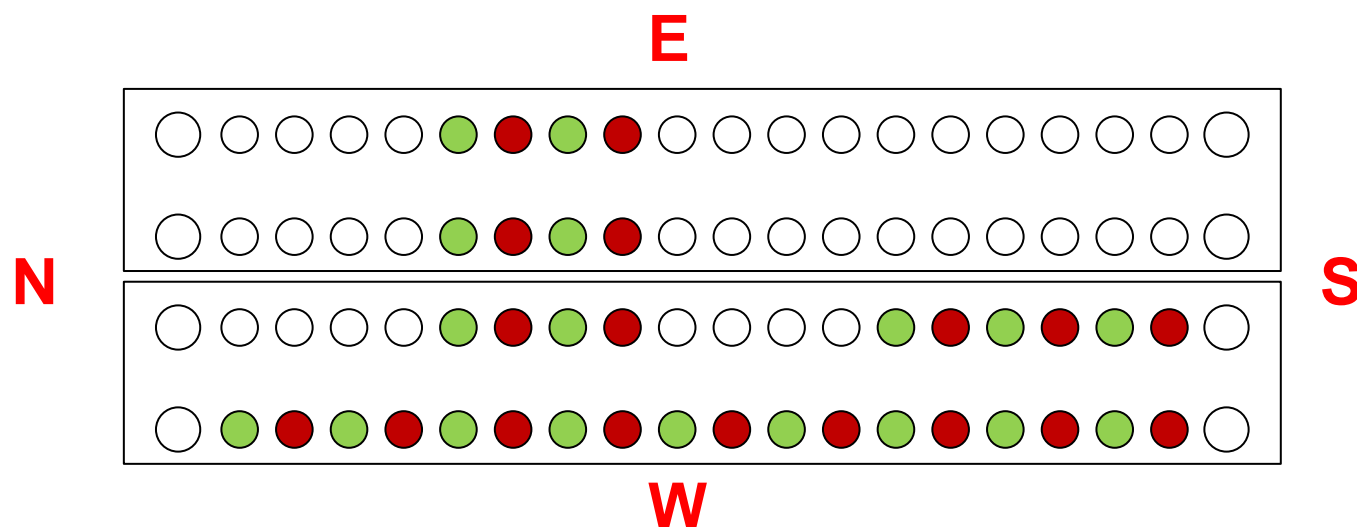

# Cable Excess Handle

- A line of 12 vertical trays have been mounted on the wall mounted behind the PMT racks.
- 8 trays are used for HV (RG58).
- 4 trays are used for signal (RG316)
- The excess cable is bent across the trays.

