


Linac Startup Status

- Received approval to run beam 01/11/2024 afternoon
- Successfully transmitted beam from Ion source through LEBT, MEBT, DTL and Transition section
 - Controller for LEBT horizontal trim LTRMH down, will be replaced next week

- Excessive losses past KRF2, appear to be losing all beam by end of Linac (no reading on D7TOR)

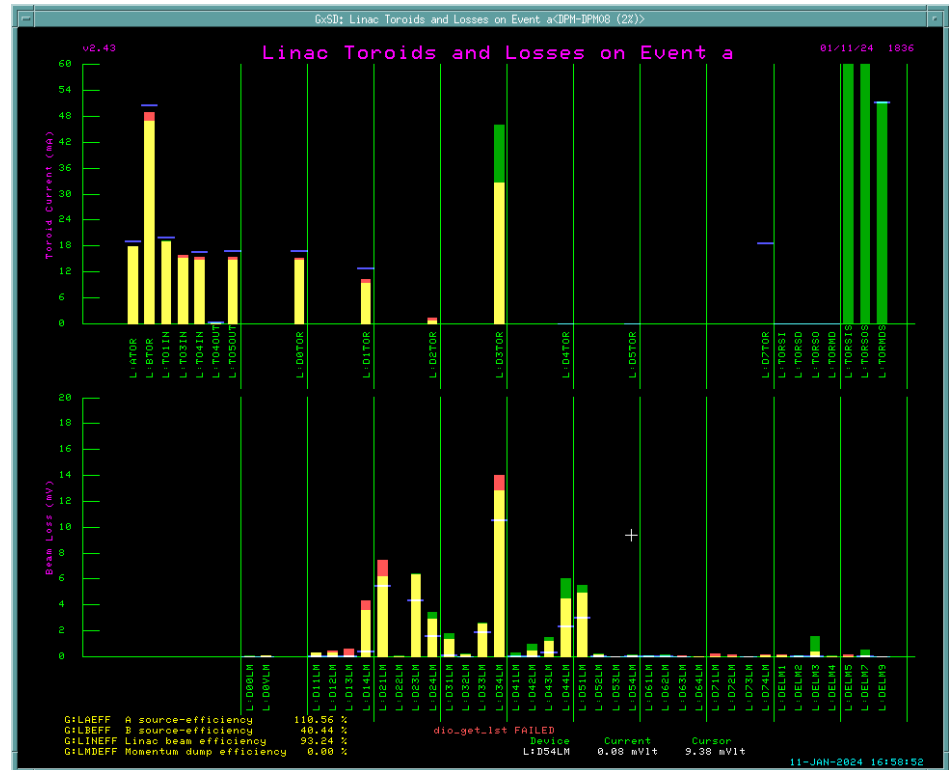

Linac Startup Status (2)

- Problem traced down to KRF2 LLRF misregulation
 - Gradient drops off when beam pulse arrives
 - Will be investigated next week

